"Music Hub"

"Your art is made for showing to the world, not for storing at your phone at all."

By Open Line Technology

Company Name : Open Line Technology (OLT)

Date : 3/4/2018

Contents

- Vision
- Mission
- Objective
- Projective plan
- Introduction and Background
- Requirement gathering process
- Work break down structure
- System design of user's view
- System design of admin's view
- Data flow diagram of User's view
- Data flow diagram of admin's view
- Project Staffing(Name and responsibilities)
- Schedule
- Communication plan
- Risk
- Conclusion

"Music Hub"

Vision

To create solution for the problems in society though technology

Mission

To make a platform for connecting new singers with audience faster

Objective

To make solution for the youth society who is interesting in music and who make production of music by creating music platform

Project Plan

Project Name Music Hub

Expected Result/product/Scope Platform for connecting new singers' songs and audience

easily

Sponsor's Name Nobody

Sponsor's Organization -

Title -

Project Duration Project Start Date : April 4, 2018

Project Finish Date : June 11, 2018

Key Schedule Milestones UI design ,frame , responsive design : April 9, 2018

Account login/logout, sign up: April 16, 2018

News feed : April 23, 2018

Follow: April 30, 2018

profile, save: May 7, 2018

payment set up, pay feature set up: May 14, 2018

review whole website: May 21, 2018

Calculate for domain, hosting cost: May 28, 2018

Search investor: June 4, 2018

Search domain, hosting, prepare for publication: June 11,

2018

Budget → Domain cost

→ hosting cost

→ Internet cost

→ advertising cost

Approaches

→ Build local site

- → set payment
- → calculate general cost for publication
- → search investor for publication
- → search partners for co-founders
- → make publication
- → make advertising for website and search investor and cofounder


Introduction & Background

Every new singer want to public to people who interest in music. So, this Music Hub,platform will help to connect between new singers and audience faster.

Requirement gathering process

- Collect tutorial for projeect
- Search for cheap domain and hosting
- search for investor
- search for co-founders with the skill the project needed

Work Break Down Structure

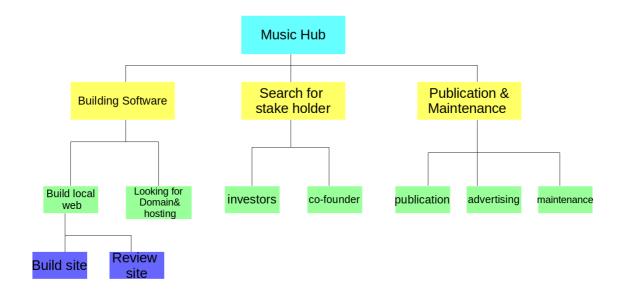

Work Break-down structure for building projects

User's view


- 1. Newsfeed
 - followed
 - o save post
- 2. Profile
 - o account sign up
 - o account login/logout
- 3. music post update
 - delete post
 - upload post
 - save post
 - report
- 4. VIP account
 - Payment set up
 - o changing VIP and normal account
- 5. Report and feedback
 - Send report to Admin
 - o send feedback to Admin

- o get notification from Admin
- get notification


Admin's View

- 1. Admin acc login/logout
 - o login Admin account
 - o logout Admin account
- 2. user accounts check
 - o check normal / payment account list
 - o delete accounts
 - o send message to user
 - o ban system
- 3. post check
 - check post list with user accounts
 - delete post
 - o add post
 - o ban system
- 4. create Admin account
 - Admin accounts lists
 - o create Admin account
- 5. Feedback and report list
 - Admin accounts list
 - send message to Admin account
 - o feedback list
 - Report list
 - Reply to user account


System design of user's view

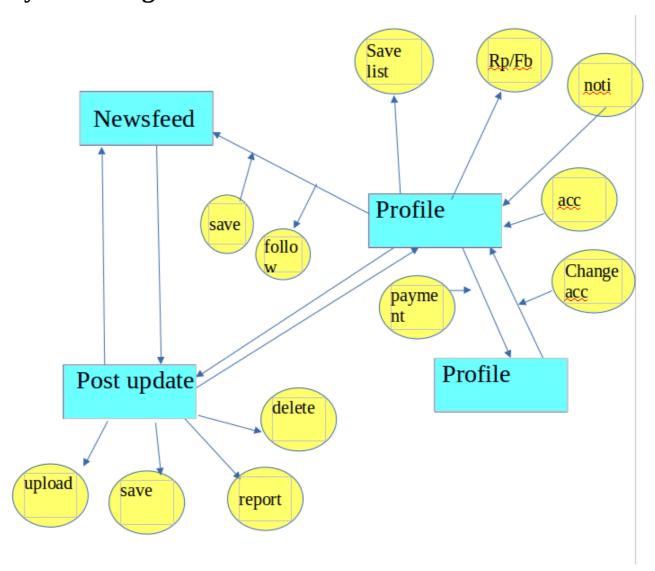


System design of Admin's view

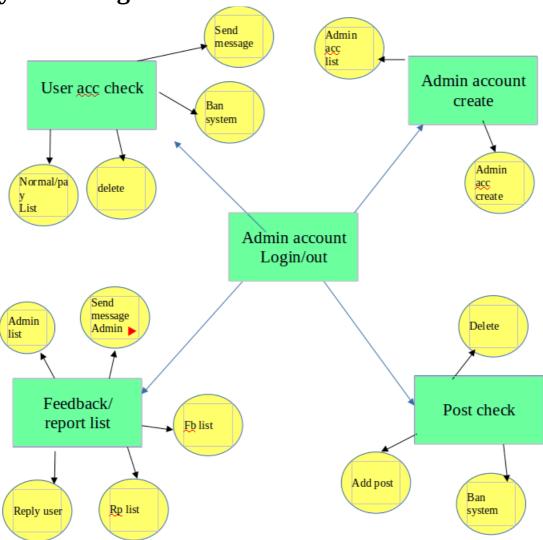

Data flow diagram of User's view

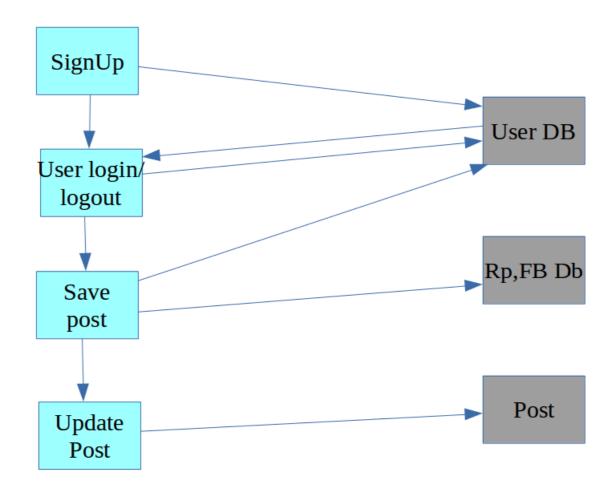

Data flow diagram of Admin's view

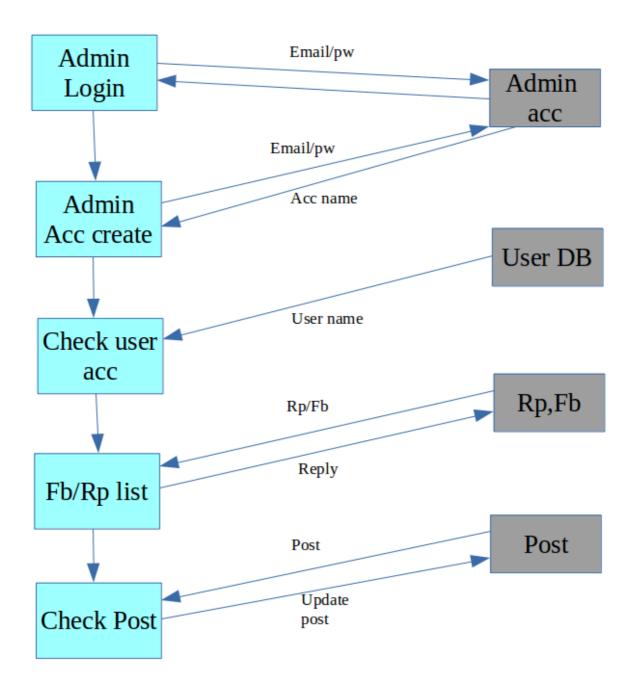

Project Staffing(Name and responsibilities)

Name	Role	Responsibility
Min Maung Maung	The Dreamer	+Monitor Project
		+plan project
		+build project
Ye Thu Win	The Hustler	+Monitor financial details
		+plan marketing
		+sell product
		+search project
Eh So Gay,	The Hacker	+Build product
Thoon Su San		+testing
		+coding

Schedule

Music Hub					
Task Name	Start Date	End Date	Duration	Assigned to	Comment
Planning			5weeks 1 day		
Planning project			3days	Dreamer	
Build project prototype			3weeks	Dreamer	
Build co-fonder			1week	Dreamer	
1 st agreement meeting			5days	Dreamer, Hustler , Hacker	
Building					
Build website			4 weeks	Dreamer,Hacker	
Search domain,hosting			1week	Dreamer, Hustler , Hacker	
Review website			1week	Dreamer,Hacker	
Implementation and Monitoring					
Search Investor			1week	Hustler,Dreamer	
Member increment			1week	Hustler,Dreamer	
Divided new members responsibilities			1week	Dreamer, Hustler , Hacker	
Review product			1week	Dreamer,Hacker	

Communication Plan

Type of Message/	Media	Frequency/	Communicatio	Responsible person
Content		Timing	n Deliverables	
Project development	Face-to-Face	weekly	Project	Hacker, Dreamer,
progress	meeting		monitoring	Hustler

			report	
Current Installation	Group chat at	Daily	Progress report	Hacker, Dreamer,
Status	facebook			Hustler
Divide Building project	Face to Face meeting	Weekly	Progress report	Hacker,Dreamer
	/ E-mail			
Project metering meeting	Face to Face meeting	As scheduled	Status report	Hacker,Dreamer, Hustler

Risk

Risk / Event	Possibility	Severity
Unstable Dollar Price	High	High if the price is too much different with estimated dollar price, otherwise, Medium
No investor	Medium	High
Labor illness	Medium	High
Hosting, domain cost increase	Low	High
Technician illness	Medium	High
Can't get co-founder	Low	Medium

Conclusion

This product is run by OLT,Open Line Technology. Dreamer is CEO and it make planning , team management and participate in building product. Hacker is CTO and it take responsibility for building project guide by Dreamer. Hustler is CSO and it responsible for selling products.
